
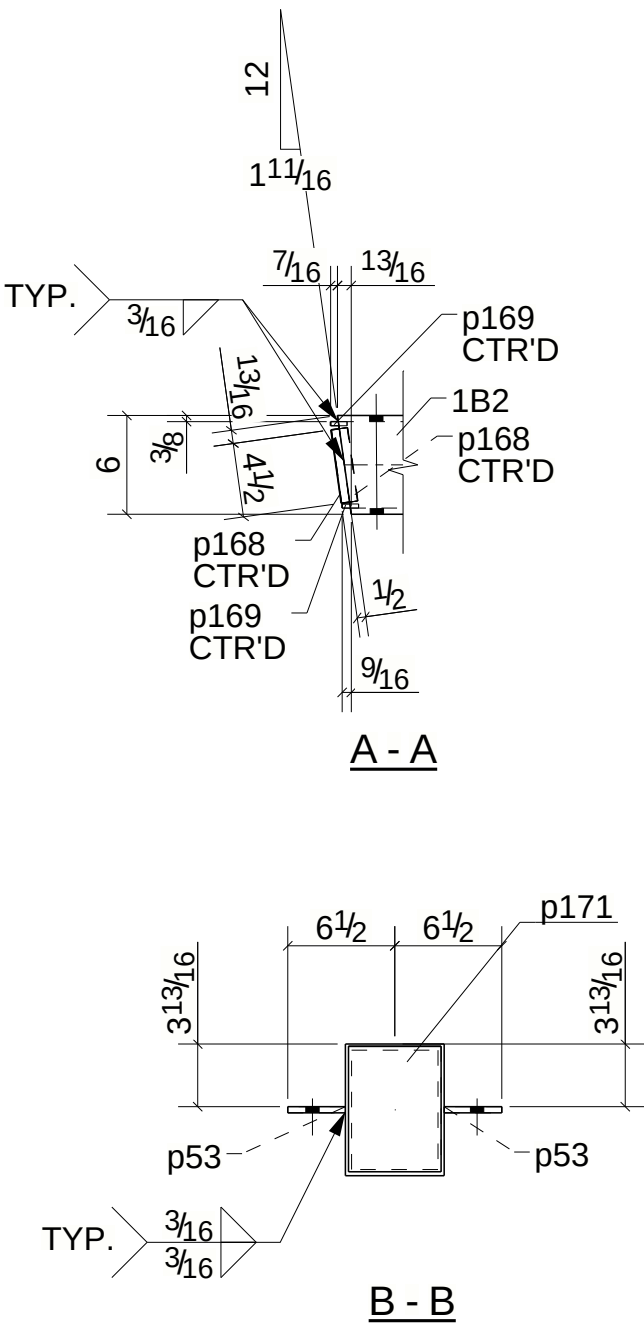


| BILL OF MATERIAL |           |               |             |              |            |            |             |
|------------------|-----------|---------------|-------------|--------------|------------|------------|-------------|
| MARK             | TOTAL QTY | SHAPE         | LENGTH      | TOTAL WEIGHT | REMARKS    | ADV MILL # | STEEL GRADE |
| 1B2              | 1         | HSS8X6X3/8    | 12'-9 9/16" | 391          | BEV-2 GALV |            | A500-GR B   |
| p53              | 2         | PL3/8"X3"     | 0'-3 1/2"   | 2            |            |            | A36         |
| p168             | 2         | PL1/4"X1"     | 0'-4 1/2"   | 1            |            |            | A36         |
| p169             | 2         | PL1/4"X1"     | 0'-6 1/2"   | 1            |            |            | A36         |
| p171             | 1         | PL1/4"X5 5/8" | 0'-7 5/8"   | 3            |            |            | A36         |

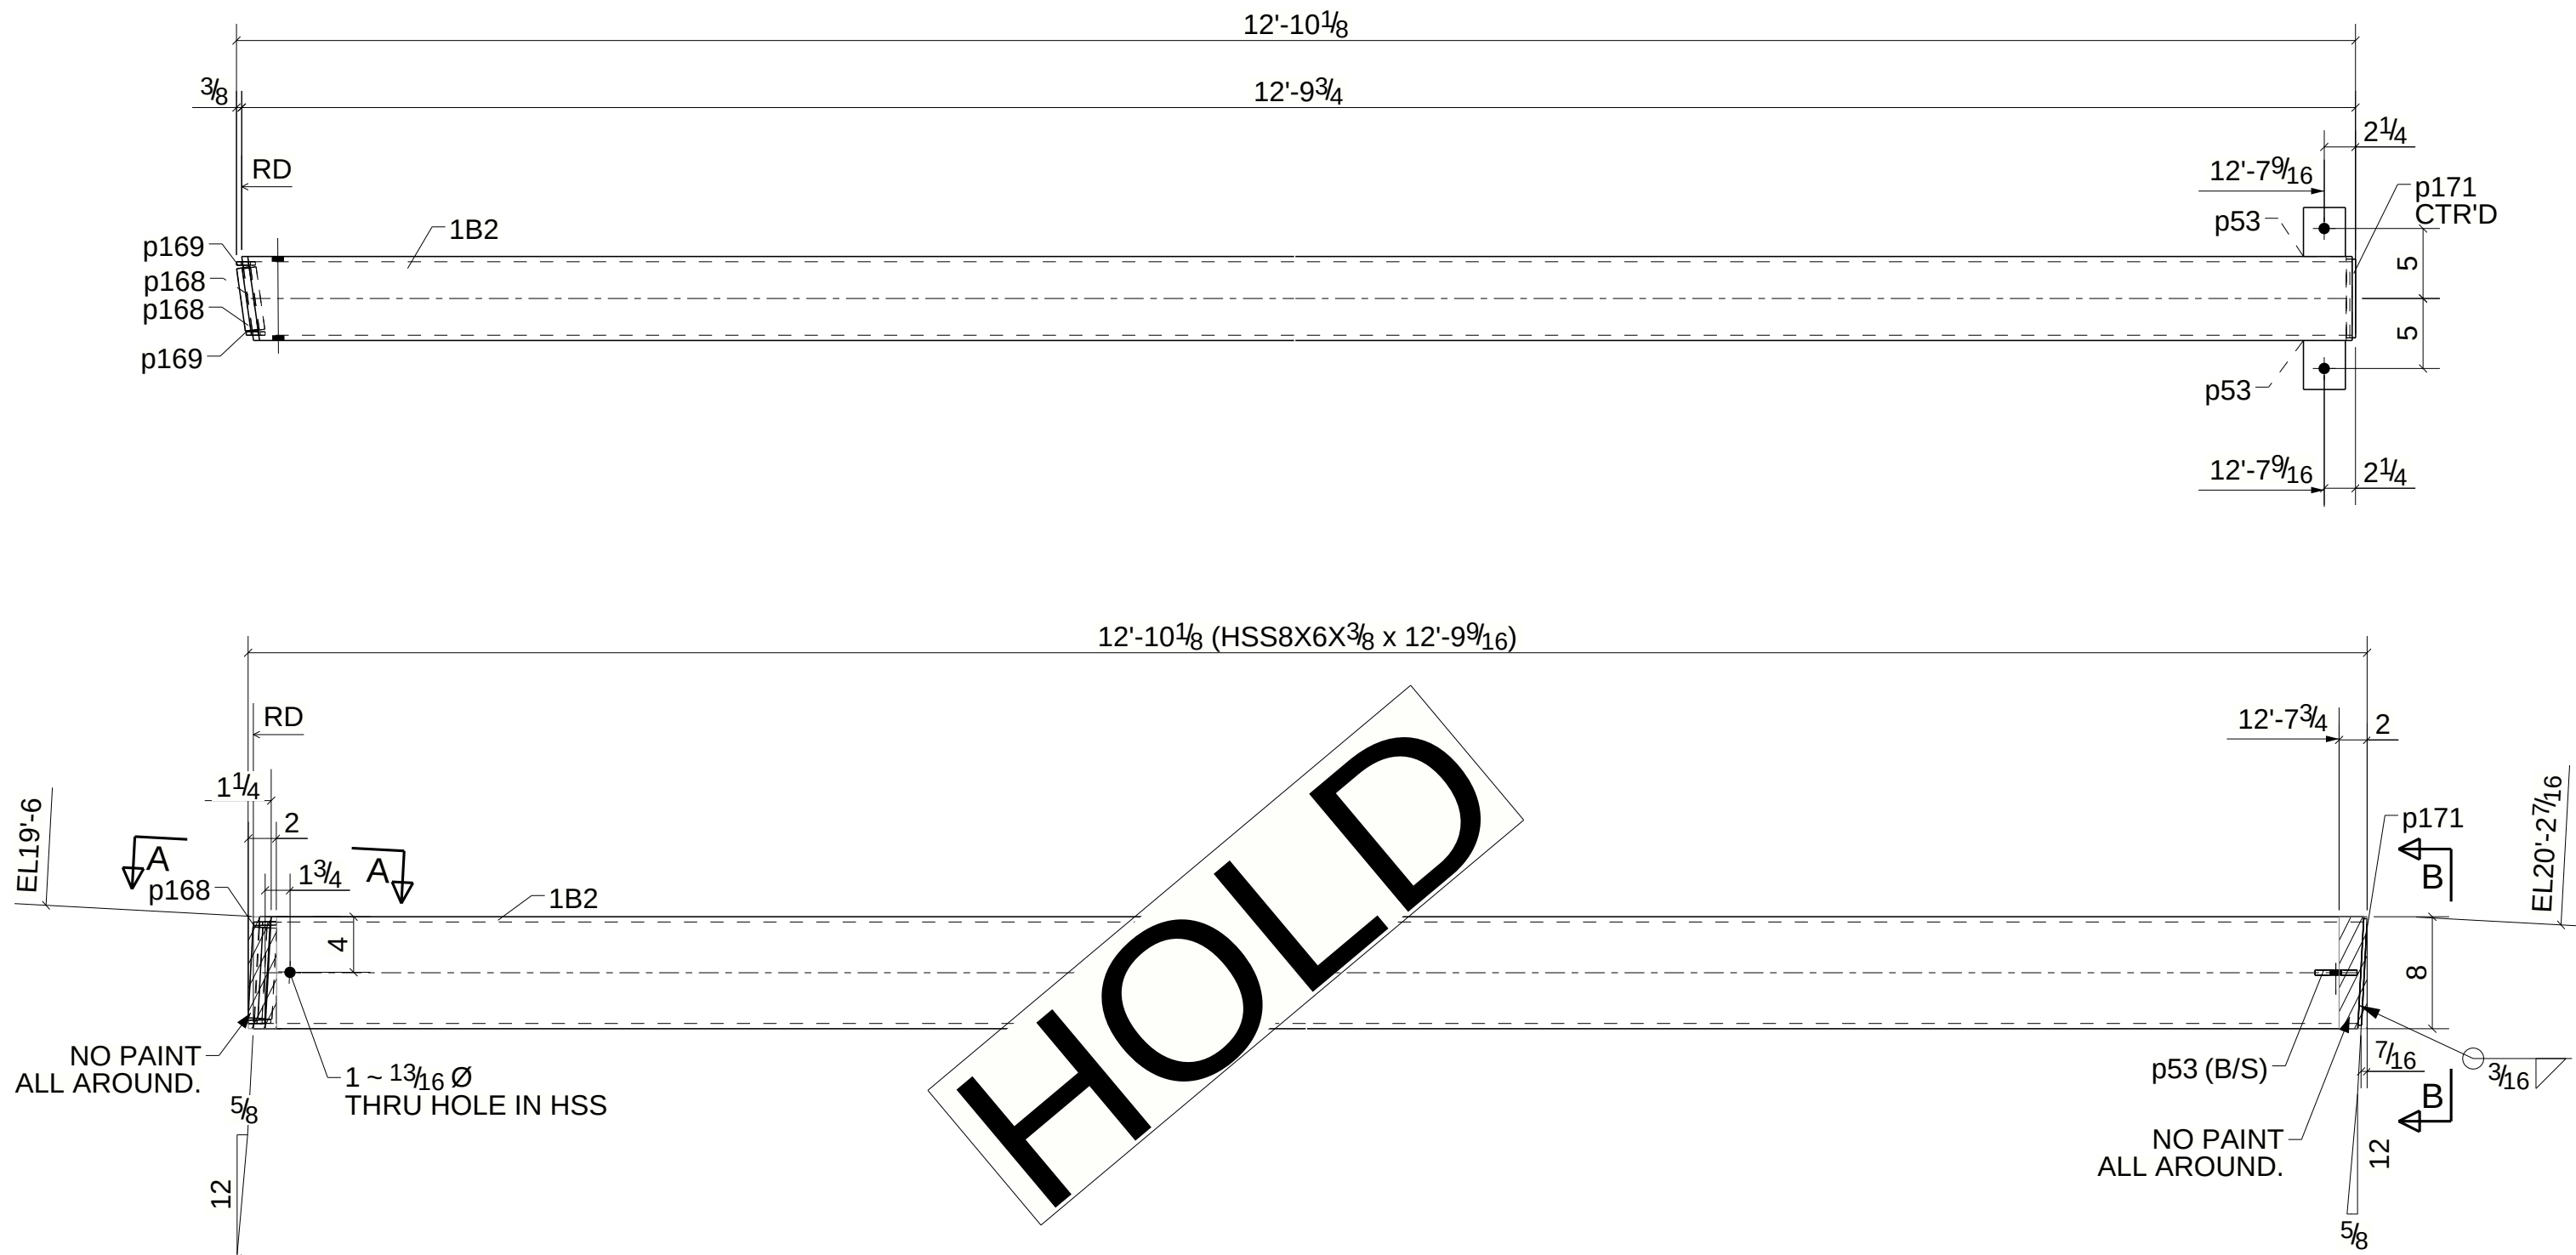

| GRID LOCATION | BOTTOM ELEVATION |
|---------------|------------------|
| 6-5/U.5-W     | 18'-10"          |

|                              |            |                 |
|------------------------------|------------|-----------------|
| 0                            | 04/11/2025 | For Fabrication |
| B                            | 03/24/2025 | For Re-Approval |
| A                            | 10/16/2024 | For Approval    |
| REV.                         | DATE       | DESCRIPTION     |
| MATERIAL<br>A36 UNO          |            |                 |
| HOLES<br>13/16 Ø UNO         |            |                 |
| WELDS<br>E70XX               |            |                 |
| SURFACE PREP.<br>SSPC SP2    |            |                 |
| PAINT NOTE<br>SW SHOP PRIMER |            |                 |

**Building  
Envelope  
Systems**



20 HIGH STREET  
PLAINSVILLE, MA 02762  
PHONE (508) 381-0429  
www.teambes.com

PROJECT NAME  
GSC JUNIPER RBP PHASE-II

LOCATION  
PARKWAY EVERETT, MA

CONTRACTOR  
BUILDING ENVELOPE SYSTEMS

DWG TITLE  
BEAM

DRAWN BY  
ABJ

CHECKED BY  
HSR

DATE DRAWN  
03/24/2025

PLT DATE  
03/24/2025

DGSTS No.  
--

REV.  
0

CONTRACT No. 24050

DWG No. 1B2

ONE - BEAM - 1B2
